Saugany Lake

April 19 Billing
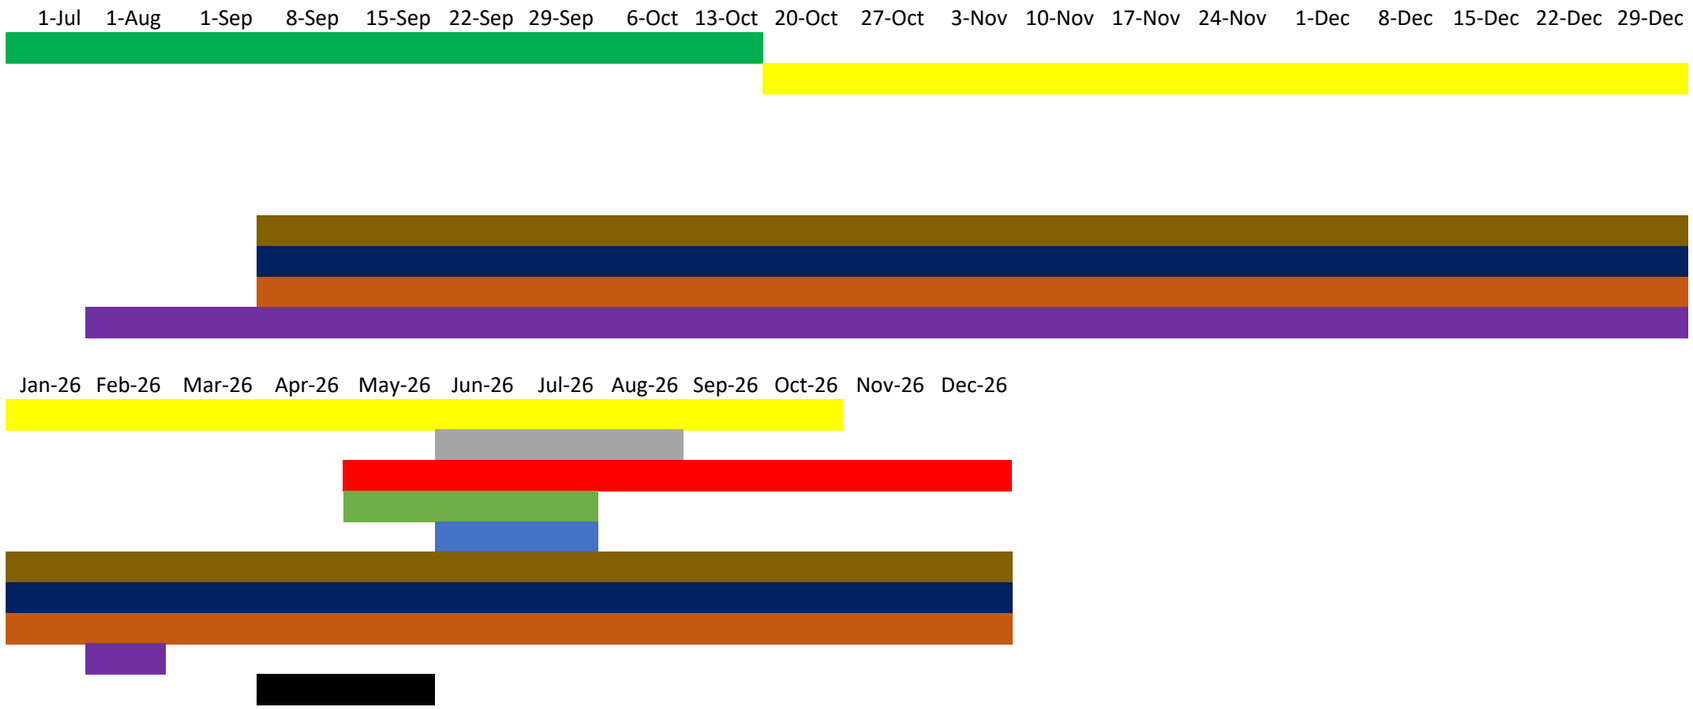
Task	% Complete
Mobilize	
12" Force Main DD	
Jack & Bore	TBD
Pump Station #7	TBD
TP #3 Flow Meter	TBD
12" Force Main OC	
Restoration	Ongoing
Erosion Control	Ongoing
MOT	Ongoing
Submittals	
2026	
12" Force Main DD	
Jack & Bore	TBD on Pothole
Pump Station #7	
TP #3 Flow Meter	Start End of April
12" Force Main OC	
Restoration	Ongoing
Erosion Control	Ongoing
MOT	Ongoing
Submittals	
Pothole RR	4-20-26 - 5-5-26
